

No: 000160

CHRISTEN INDUSTRIES, INC.
1048 SANTA ANA VALLEY ROAD
HOLLISTER, CALIFORNIA 95023
TELEPHONE: (408) 637-7405

By: IC

Date: 04-29-80

Page: 1 of 1

Send To: 904 FUSELAGE KIT

C-0002

C CHRISTEN INDUSTRIES INC.
U 1048 SANTA ANA VALLEY RD.
S HOLLISTER, CA 95023
T

Subject: INSPECTION OF EAGLE II
AIRCRAFT 904 FUSELAGE
STRUCTURE FOR PRESENCE
OF TUBULAR ELEMENTS


Recent factory inspection activities indicate that there is a possibility that your 904 fuselage structure may have been manufactured with two small tubular elements omitted from the landing gear attach area.

Please inspect your fuselage structure in accordance with the attached Engineering Sketch 90117 to verify the presence of the two 3/8 diameter tubes which are located immediately aft of the forward wing attach fittings as indicated by the arrows.


If the tubes are not present on your fuselage structure, please telephone the Christen factory collect to arrange for corrective action.

Enclosures:

1 EA Engineering Sketch X-90117

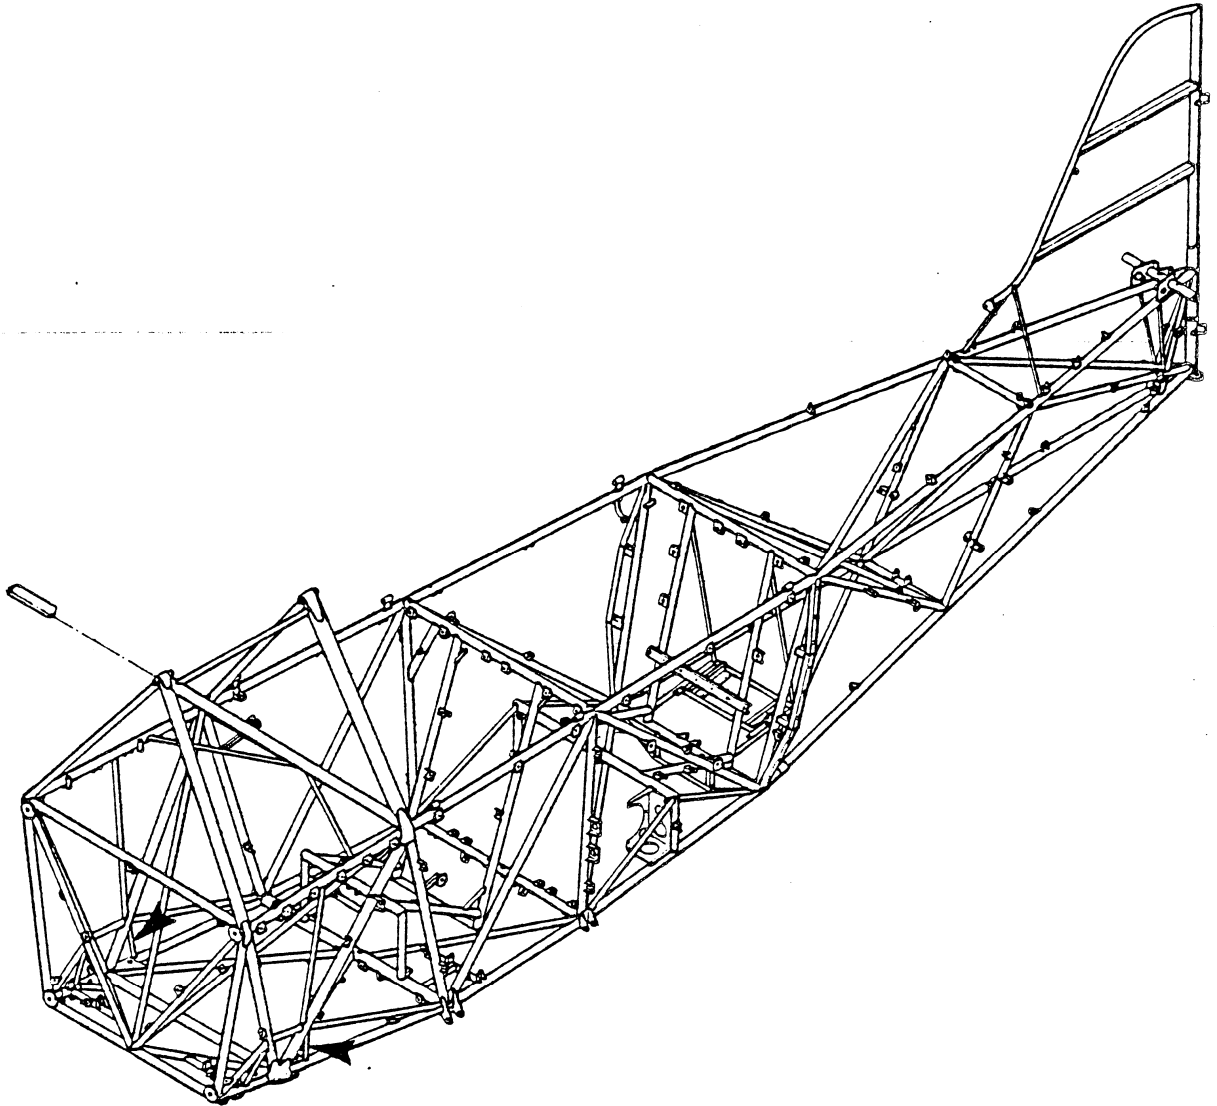

VERIFY THAT THE REINFORCEMENT TUBES
 MARKED WITH AN ARROW HEAD ARE ATTACHED

UNLESS OTHERWISE SPECIFIED: TOLERANCES: FRAC. \pm 1/64 DEC. XXX \pm .005 ANGLES \pm 0° 30' DIMENSIONS IN INCHES DO NOT SCALE DRAWING	MATERIAL AND CONDITION NOTED		CHRISTEN  CHRISTEN INDUSTRIES HOLLISTER, CALIFORNIA		
	FINISH NONE				ENGINEERING SKETCH
DRAWN BY V. CLSDG	DATE 4-28-80	PROJECT EAGLE II AIRCRAFT		TITLE FUSELAGE INSPECTION	
APPROVED BY	DATE			CODE NO. X-90017	ISSUE
